

# Architect's Observation Report

Report: 12  
Date: August 12, 2014  
Time: 3:18 pm  
Temp: 77 Degrees  
Weather: Mostly Clear



**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

---

Project: 13-0639 – Edina Sports Dome and Ice Rink  
Owner: City Of Edina  
Architect: Cunningham Group Architecture Inc.  
Copy To: File

---

**Conformance with Schedule: On Schedule**

**Present at Site (Observed):**

---

<input checked="" type="checkbox"/> Dale Michalek(RJM)	<input checked="" type="checkbox"/> Ann Kattreh
<input checked="" type="checkbox"/> Dan Mehok (RJM)	<input checked="" type="checkbox"/> Susie Miller (City of Edina)
<input checked="" type="checkbox"/> Gerhardt Gliedge (RJM)	<input checked="" type="checkbox"/> Eric Boettcher (City of Edina)
<input checked="" type="checkbox"/> Rob Madden (Muska)	<input checked="" type="checkbox"/> Amanda Holle (City of Edina)
<input checked="" type="checkbox"/> Wyatt Gutzke (New Look PM)	<input checked="" type="checkbox"/> Peter Saabye (City of Edina)
<input checked="" type="checkbox"/> Brad Werner (Kelleher PM)	<input checked="" type="checkbox"/> Tunde Olusanya (CGA)

---

**Cunningham Group  
Architecture, Inc.**

St. Anthony Main  
201 Main Street SE  
Suite 325  
Minneapolis, MN  
55414

Tel: 612 379 3400  
Fax: 612 379 4400

---

## WORK IN PROGRESS

---

1. Dome grade beam has been poured including dome anchor, drains and channel; all that remains of dome concrete work are the stoop concrete slabs.



[www.cunningham.com](http://www.cunningham.com)



**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*





**CUNNINGHAM  
G R O U P**

*AIA Minnesota  
Firm Award Recipient*





**CUNNINGHAM  
G R O U P**

*AIA Minnesota  
Firm Award Recipient*



2. Storage building footings have been poured and cured, foundation wall concrete and footing foundation wall was poured today (08/12/14) and is still curing.





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*



3. Grade beam interior grading set at bottom of dome drainage system is currently in progress.



**CUNNINGHAM  
G R O U P**

*AIA Minnesota  
Firm Award Recipient*



4. Staking for accessory building in preparation for installation of the Accessory building footing.





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*


5. Steel decking for ice rink roof deck installation is scheduled to be completed Thursday August 14, 2014.





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

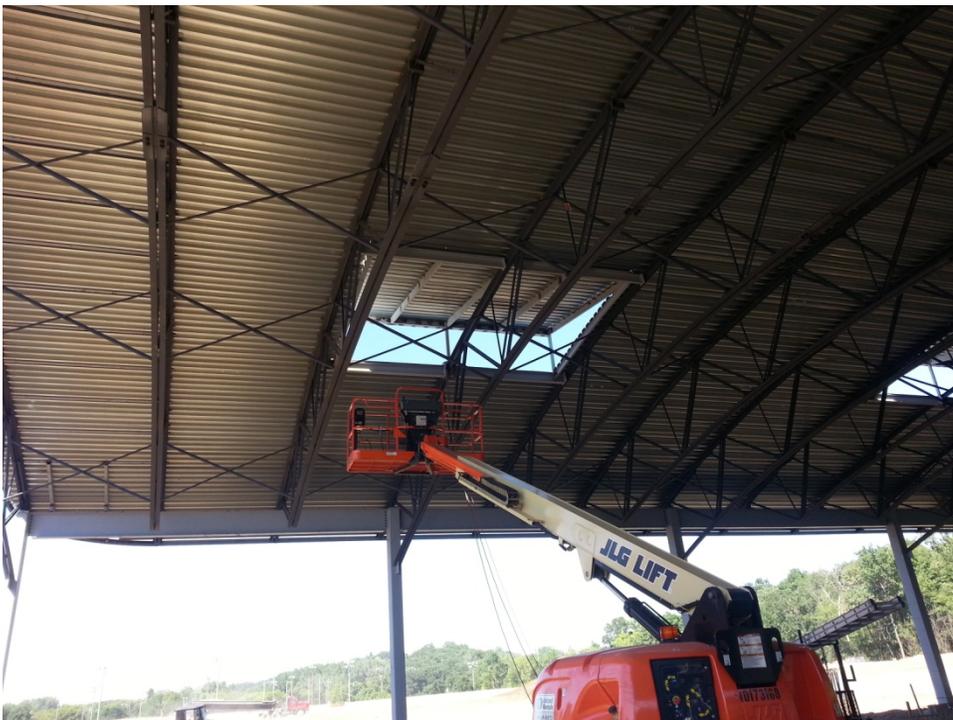




**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

6. Demolition in Refrigeration room has begun and is scheduled to be complete at the end of the week; Friday August 15, 2014.

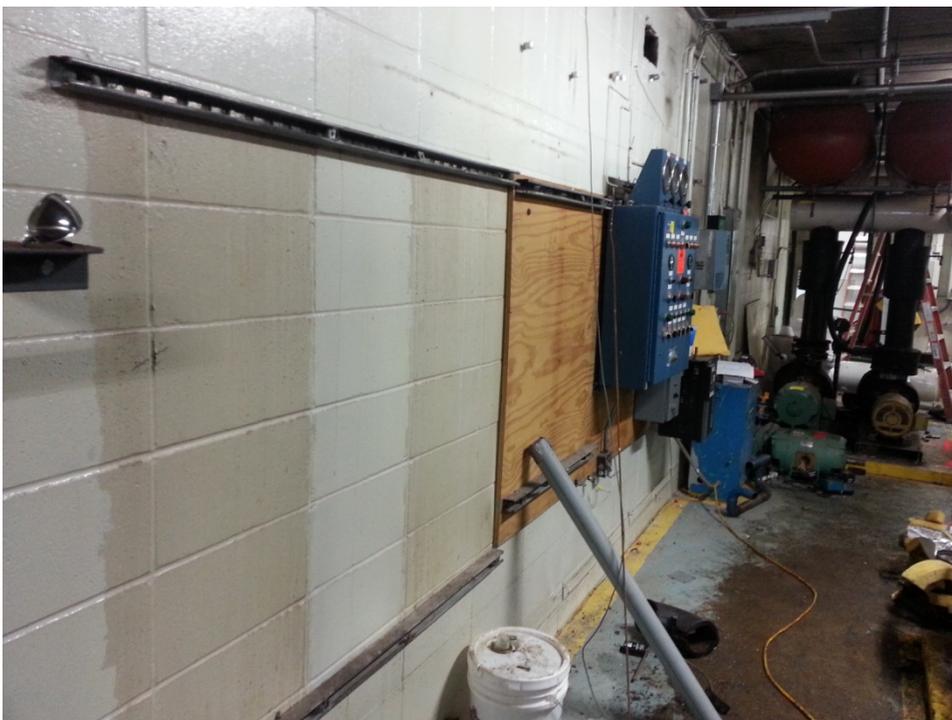



**CUNNINGHAM  
GROUP**

*AIA Minnesota  
Firm Award Recipient*





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

7. Analysis of north wall of east arena Refrigeration Room has been analysed, abatement will be required, abatement work is scheduled to begin on Wednesday August 13, 2014.



#### **INFORMATION OR ACTION REQUIRED**

---

1. Documentation for the East Arena Mechanical Plaza proposal request is in progress.

**END OF OBSERVATION REPORT 12**
