

Architect's Observation Report

Report: 16
Date: September 9, 2014
Time: 2:51 pm
Temp: 73 Degrees
Weather: Cloudy



CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*

Project: 13-0639 – Edina Sports Dome and Ice Rink
Owner: City Of Edina
Architect: Cunningham Group Architecture Inc.
Copy To: File

Conformance with Schedule: On Schedule

Present at Site (Observed):

<input checked="" type="checkbox"/> Dale Michalek(RJM)	<input checked="" type="checkbox"/> Ann Kattreh
<input checked="" type="checkbox"/> Dan Mehok (RJM)	<input checked="" type="checkbox"/> Susie Miller (City of Edina)
<input checked="" type="checkbox"/> Gerhardt Gliège (RJM)	<input checked="" type="checkbox"/> Eric Boettcher (City of Edina)
<input checked="" type="checkbox"/> Rob Madden (Muska)	<input checked="" type="checkbox"/> Amanda Holle (City of Edina)
<input checked="" type="checkbox"/> Wyatt Gutzke (New Look PM)	<input checked="" type="checkbox"/> Dave Green (Yeadon)
<input checked="" type="checkbox"/> Brad Werner (Kelleher PM)	<input checked="" type="checkbox"/> Tunde Olusanya (CGA)

**Cunningham Group
Architecture, Inc.**

St. Anthony Main
201 Main Street SE
Suite 325
Minneapolis, MN
55414

Tel: 612 379 3400
Fax: 612 379 4400

WORK IN PROGRESS

1. 24" sand sub base grading is ongoing over completed dome water retention system. Sand is currently getting set and graded within the dome, granite and trap rock porous aggregate have been delivered to the site.



www.cunningham.com



CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*





CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*

2. Trench for 8" slotted collector pipe has been dug on north, south and east sides of dome ready for install.



3. Dome metal channel has been notched at drain channels to allow water to drain out of grade beam.





CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*

4. Football post footings in dome have been poured, remainder athletic footings will be poured after trap rock and gravel installation.





CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*

5. Accessory building CMU wall installation progression is slightly behind schedule, work is progressing steadily and should be complete Friday 12, September.





**CUNNINGHAM
G R O U P**

*AIA Minnesota
Firm Award Recipient*





**CUNNINGHAM
G R O U P**

*AIA Minnesota
Firm Award Recipient*





CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*

6. Structural steel members, deck and joists have been delivered and stored on site.





**CUNNINGHAM
G R O U P**

*AIA Minnesota
Firm Award Recipient*



7. Personnel airlock between dome and accessory building slab has been completely poured.






CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*

8. Storage building steel joists and roof deck have been installed; underground conduits to stub-ups have also been installed.

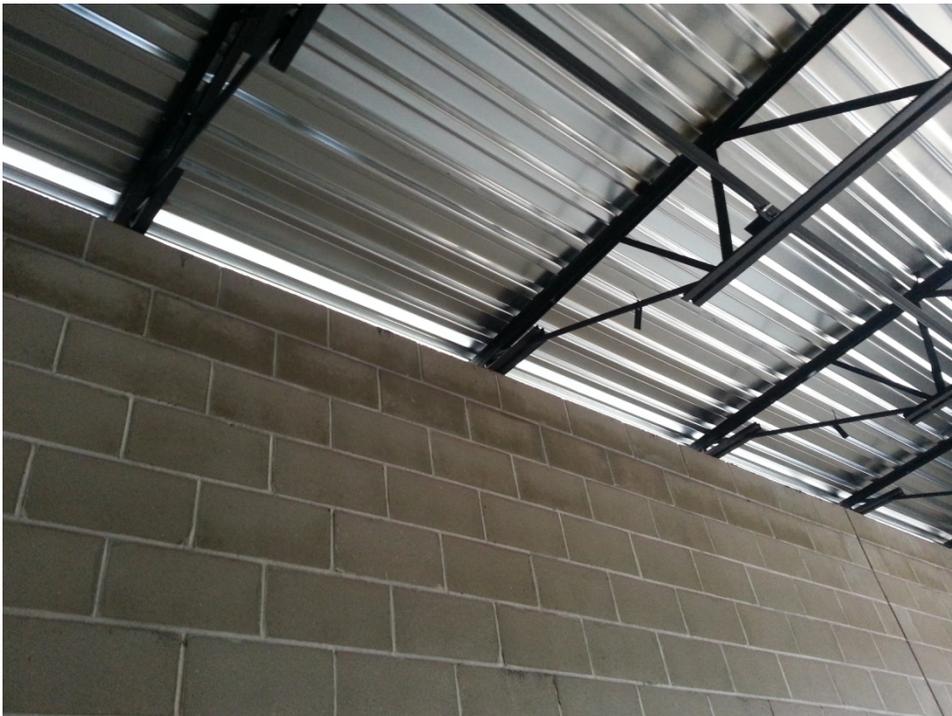



CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*





CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*

9. Ice rink canopy conduit installation for lights and speaker system is currently in progress and is scheduled to be completed on Wednesday September 10, 2014.





CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*

10. Pipes are currently being set in trench at north face of East Arena wall for the poly transmission main lines from the exterior ice rink to the refrigeration room pipe holes have been cored in rink foundation wall and the wall of the East Arena refrigeration room has been cut to allow piping through.






CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*



11. Slab cut in refrigeration room has been excavated for sub grade piping installation, some of which has already occurred; general demolition work continues.

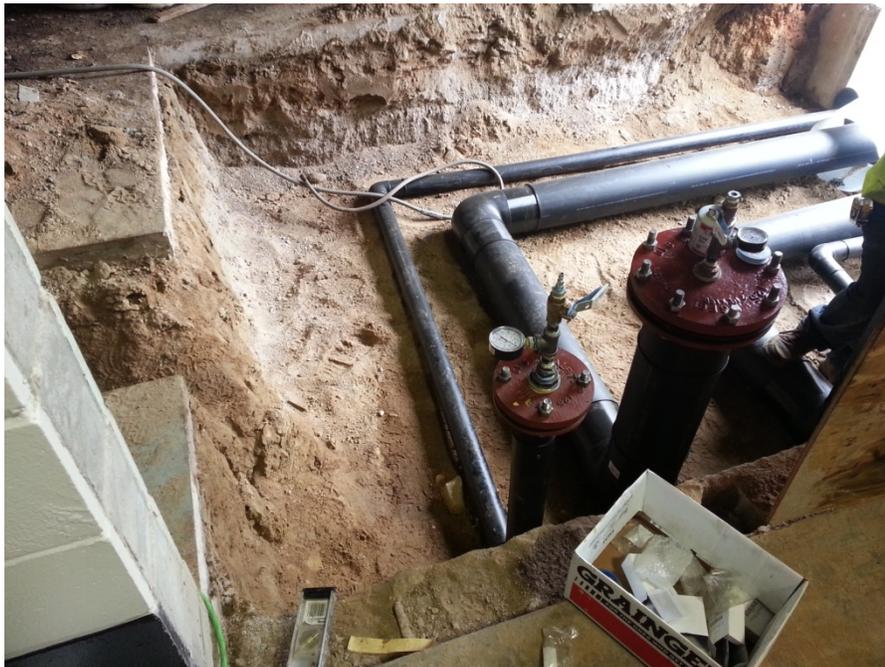



**CUNNINGHAM
G R O U P**

*AIA Minnesota
Firm Award Recipient*





**CUNNINGHAM
G R O U P**

*AIA Minnesota
Firm Award Recipient*



INFORMATION OR ACTION REQUIRED

1. Ice melt pit outside exterior ice rink design is pending - CGA to issue drawings.
2. Civil revisions to PR 08 for the east arena mechanical plaza waterproofing pending approval.
3. Asbestos abatement work for resilient flooring adhesive in East Arena pending.
4. Some field light locations conflict with water and storm lines along the west side of the dome, new locations are to be proposed by RJM, for review by the design team.
5. East Arena shoring drawings need to be submitted to the City of Edina.

END OF OBSERVATION REPORT 16
