



May 29, 2015

Countryside H Neighborhood Roadway Improvements


Dear Resident:

Private Utility Reconstruction Schedule:

- Gas (CenterPoint Energy) Update:
 - CenterPoint Energy's subcontractor has finished work in the neighborhood. Restoration efforts in areas that are not affected by the City's reconstruction project should begin soon. Restoration of the remaining disturbed lawn areas within the right-of-way will be completed later this year as part of the neighborhood reconstruction project.
- Xcel Energy
 - Crews will continue to mobilize in the coming weeks to move conflicting power poles and street lights as needed. Street lights on stage I will be replaced in the same approximate locations.

Project Schedule:

This project is being completed in stages. For your reference, here is the staging plan for the project:

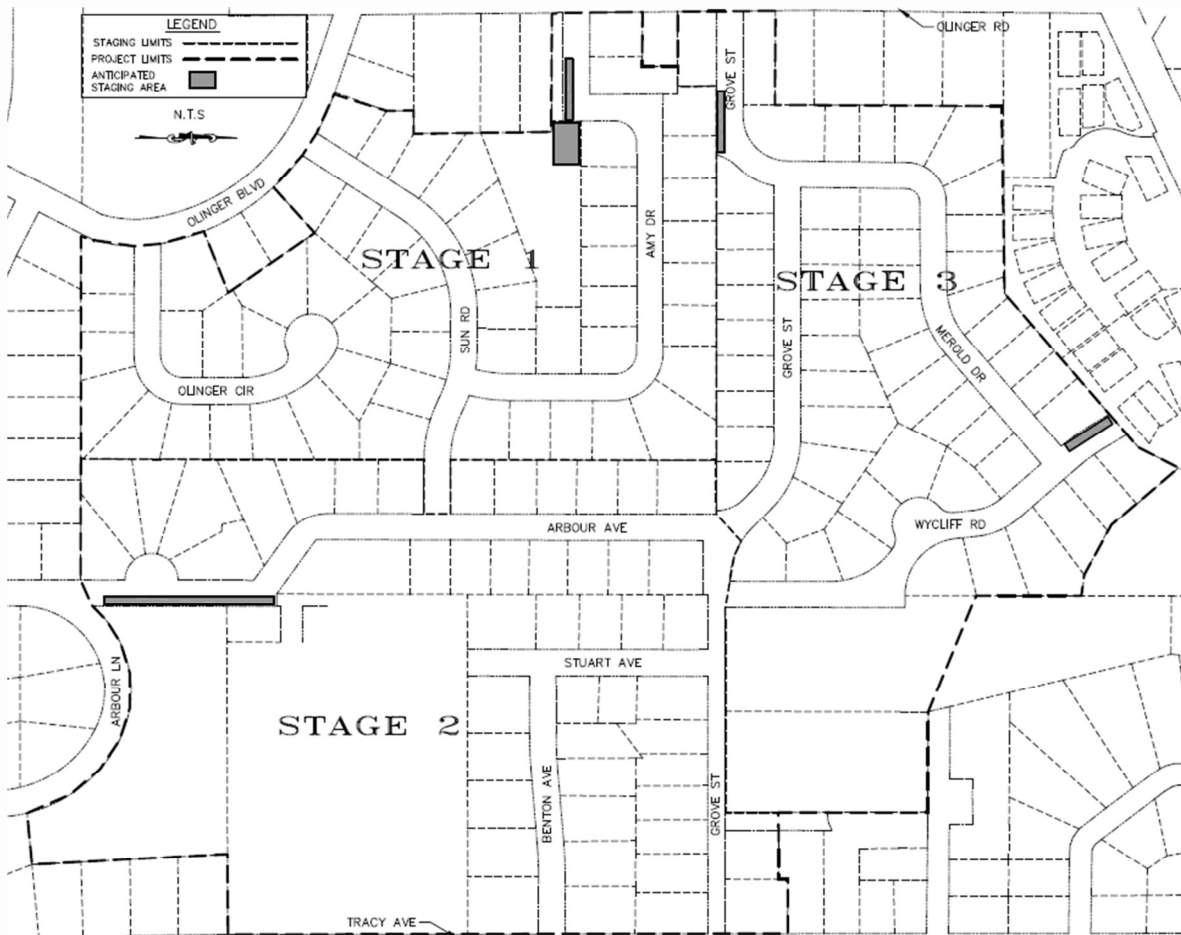

ENGINEERING DEPARTMENT

7450 Metro Boulevard • Edina, Minnesota 55439
www.EdinaMN.gov • 952-826-0371 • Fax 952-826-0392

Stage 1 includes Olinger Circle, Sun Road and Amy Drive. Stage 2 includes Arbour, Benton and Stuart avenues and Grove Street east of Arbour Avenue. Stage 3 includes Merold Drive, Wycliffe Road and Grove Street west of Arbour Avenue.

Crews have completed sub-cutting the road which involves digging the road and ensuring there is good base material on which to construct the new roadway. This is compacted and gravel will be laid over the top of it. A similar process has begun for the sidewalk along Sun Road.

Crews have removed portions of curb that have settled or badly cracked and will maintain driveway access by creating a gravel ramp to your driveway. Concrete workers are scheduled to replace the curbs and other concrete work beginning early next week. Please refrain from putting names, initials, footprints, etc. in the new concrete. Portions with this will be removed and replaced.

During this work, the contractor will let you know if you will be unable to access your driveway for the day. Residents trying to access their driveways may be required to enter the street from the opposite side that you normally would, at times. We appreciate your understanding and cautious driving.

With the concrete work next week, there may be days that your driveway will not be accessible. Please look for notices left at your front door and make sure your vehicles are out of your driveway/garage and properly re-located if you have a need for them over that time period. If you have any special mobility needs during this time period, please let me know and we will do our best to help out in any way we can.

The contractor has installed the drain tile and a subcontractor has completed installation of sump drains throughout Stage 1 of the project.

Stage 2 is scheduled to begin after school is out, the week of June 1.

Remember to routinely check your front door for time sensitive notices. All schedules are weather-dependent and are subject to change.

Communications:

Please contact me if you have any questions or comments regarding this project. You can reach me at 952-826-0444 or bfisher@EdinaMN.gov. For more information about emergencies, non-emergencies and site safety, or what to do when you have special events or home improvement projects planned, visit www.EdinaMN.gov/countryside_h.

Please encourage your neighbors to sign up for City Extra, as this will be our primary means of communication throughout the project. Visit www.EdinaMN.gov/CityExtra for more information.

The City of Edina and Northwest Asphalt thank you in advance for your patience and cooperation throughout the project.

Regards,

Brad Fisher
Engineering Technician
