

# Architect's Observation Report

Report: 23  
Date: November 18, 2014  
Time: 2:08 pm  
Temp: 15 Degrees  
Weather: Light snow and wind



*AIA Minnesota  
Firm Award Recipient*

---

Project: 13-0639 – Edina Sports Dome and Ice Rink  
Owner: City Of Edina  
Architect: Cunningham Group Architecture Inc.  
Copy To: File

---

**Conformance with Schedule:** On Schedule (with some adjustments)

**Present at Site (Observed):**

---

|  |  |
|--|--|
| <input checked="" type="checkbox"/> Dale Michalek(RJM)     | <input checked="" type="checkbox"/> Ann Kattreh (City of Edina)  |
| <input checked="" type="checkbox"/> Dan Mehok (RJM)        | <input checked="" type="checkbox"/> Susie Miller (City of Edina) |
| <input checked="" type="checkbox"/> Gerhardt Gliedge (RJM) | <input checked="" type="checkbox"/> Eric Boettcher               |
| <input checked="" type="checkbox"/> Paul Koliass (RJM)     | <input checked="" type="checkbox"/> Rob Madden (Muska)           |
| <input checked="" type="checkbox"/> Thomas Hussong         | <input checked="" type="checkbox"/> Steve Flanagan (Yeadon)      |
| <input checked="" type="checkbox"/> Mike Rouse (Horowitz)  | <input checked="" type="checkbox"/> Tunde Olusanya (CGA)         |

---

Cunningham Group  
Architecture, Inc.

St. Anthony Main  
201 Main Street SE  
Suite 325  
Minneapolis, MN  
55414

Tel: 612 379 3400  
Fax: 612 379 4400

---

## WORK IN PROGRESS

---

1. Dome interior installation is ongoing; all the light fixtures have been mounted and fixture wiring is currently being run between dome membranes in tandem with bubble wrap insulation.



[www.cunningham.com](http://www.cunningham.com)



**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

Vehicular Airlock installation is still in progress overhead doors remain to be installed.






**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*



Dome Light fixture

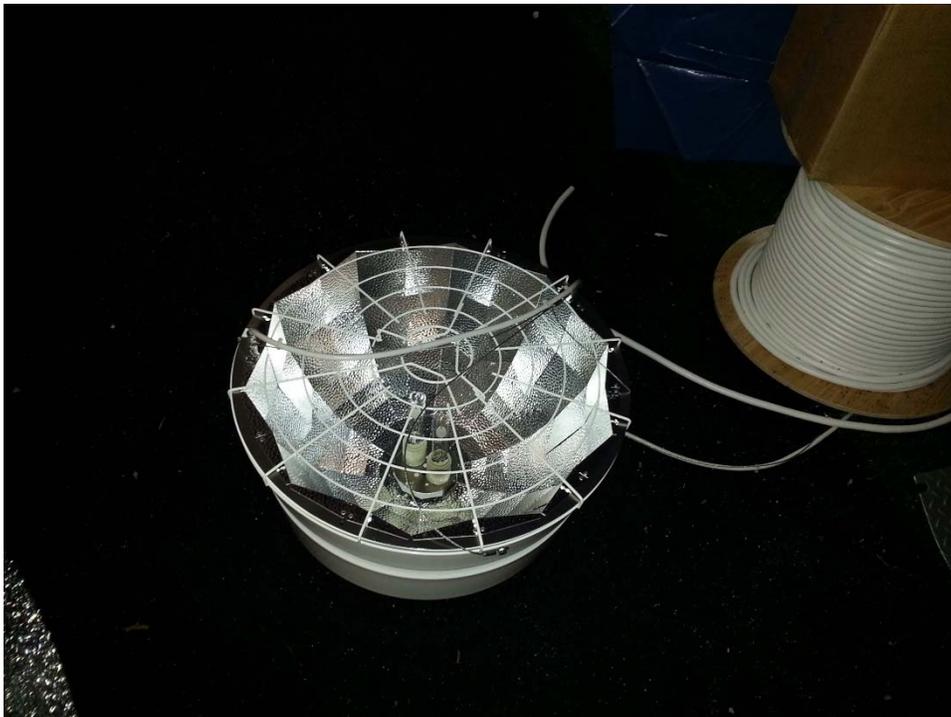



**CUNNINGHAM  
G R O U P**

*AIA Minnesota  
Firm Award Recipient*

Rolls of bubble wrap insulation





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

Dome equipment enclosure installation with Air Handling unit backup generator and electrical and data panels



2. Accessory building exterior soffit installation progress is ongoing, plywood fully installed and flat seam metal panel over vapor barrier.





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

3. Access panel installation in drywall ceilings in the Accessory building has begun; taping and sanding for the drywall ceilings is in progress and is scheduled to be complete Thursday the 20<sup>th</sup> of November. HVAC duct sheet metal installation is in progress and will continue through to the end of the week.





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*



View from Entry vestibule (not yet installed)





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

Security Grille Track has been installed





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*



Distribution Panels, Lighting Control Panels and Fire Alarm Control Panels



T




**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

HVAC unit mounted in Mechanical room



Gas water heater has been installed in Accessory building Mechanical room

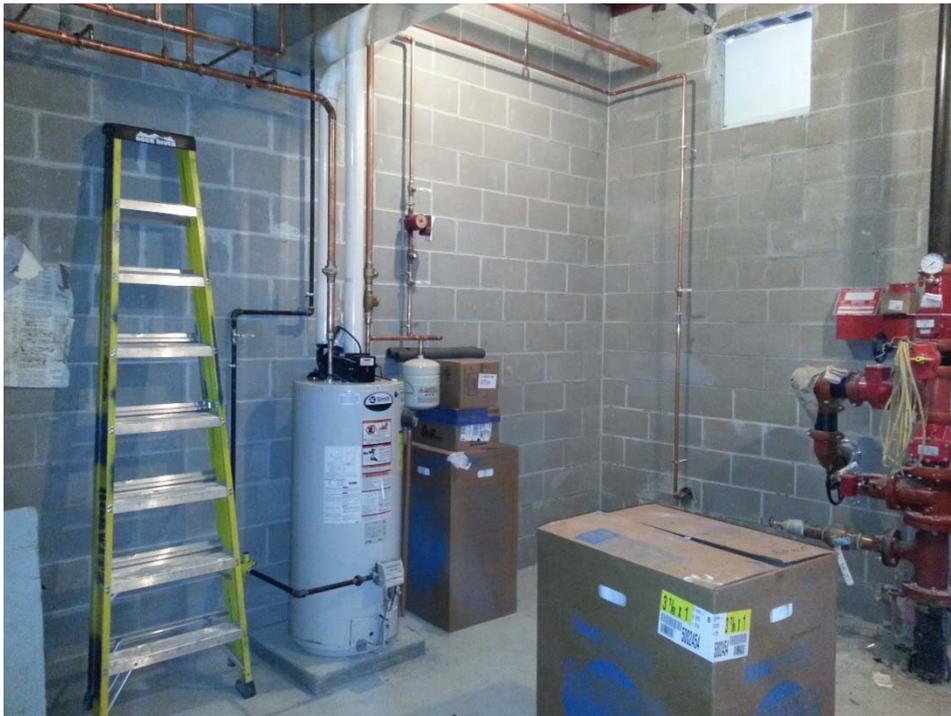



**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

4. East Arena restroom wall tile installation on women's south wall is in progress; extensive sheet metal rough-in, masonry, electrical, fire protection and door panel and hardware work is in progress through the week.





**CUNNINGHAM**  
G R O U P


*AIA Minnesota  
Firm Award Recipient*





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

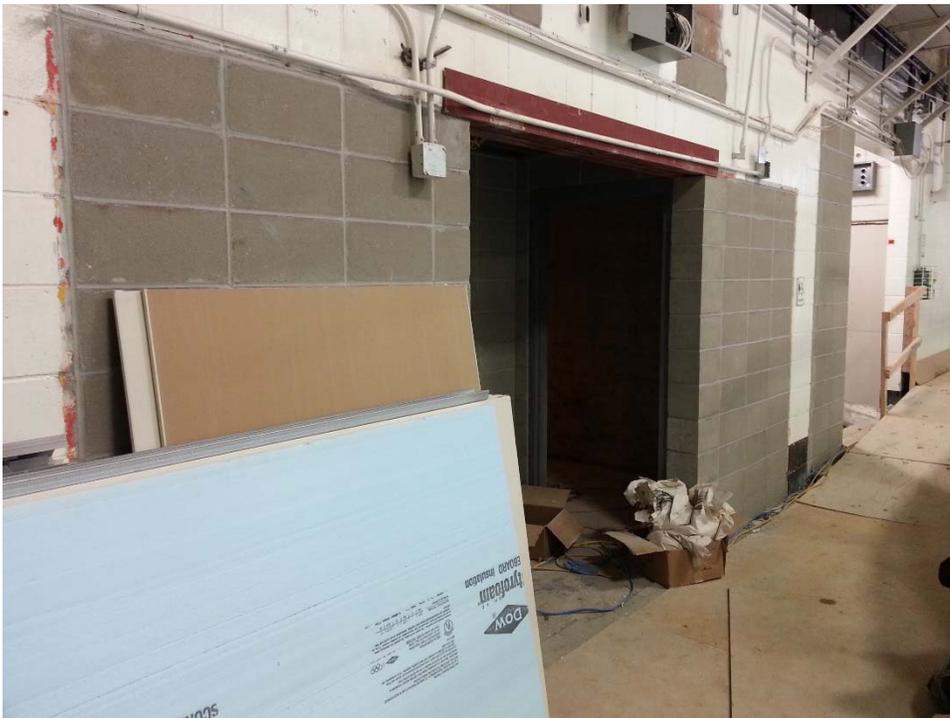



**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*


Team rooms





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

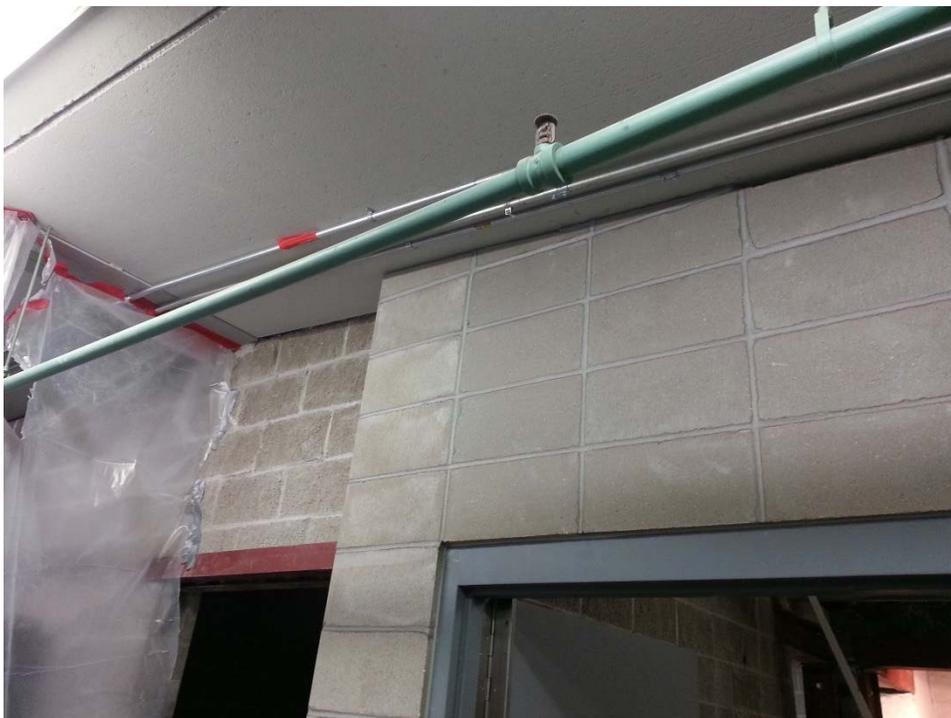



**CUNNINGHAM  
GROUP**

*AIA Minnesota  
Firm Award Recipient*





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*






**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

View from ice skaters locker room



**\*\* New storage room new concrete floor has been poured\*\***

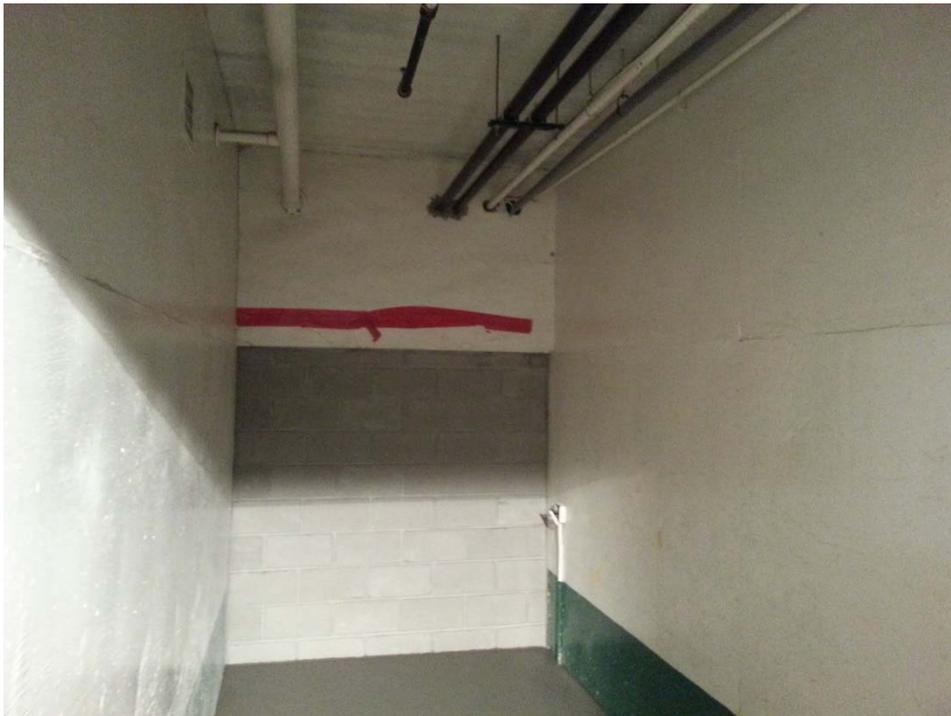



**CUNNINGHAM  
GROUP**

*AIA Minnesota  
Firm Award Recipient*





**CUNNINGHAM  
GROUP**

*AIA Minnesota  
Firm Award Recipient*



5. Work in East Arena refrigeration room continues on through the week






**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

Intake duct to mechanical plaza

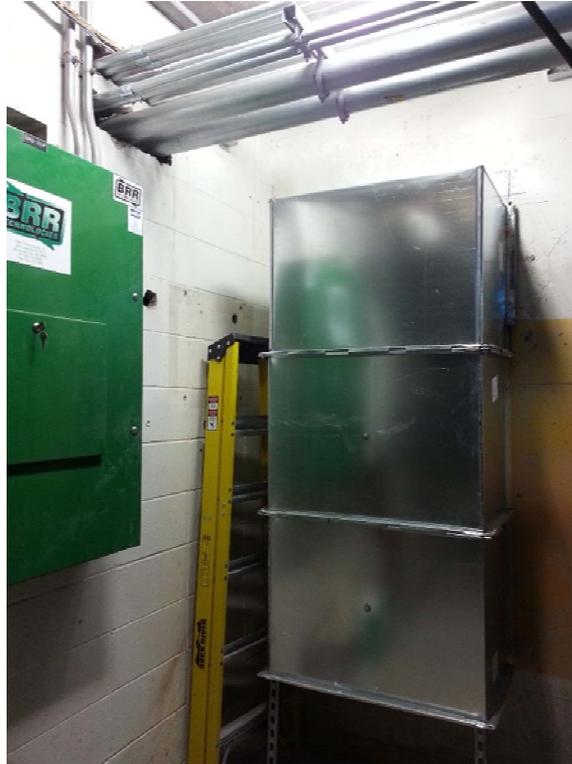



**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

6. Outdoor ice rink slab cover has been removed and dasher board installation is almost complete, standing seam metal roof on canopy is 85% complete.





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*





**CUNNINGHAM  
GROUP**

*AIA Minnesota  
Firm Award Recipient*





**CUNNINGHAM  
G R O U P**

*AIA Minnesota  
Firm Award Recipient*



7. Scoreboard wall CMW installation between Ice rink and dome is currently ongoing; wall has been covered in a heated poly tent to allow installation to continue.





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

8. Storage building roof installation is complete all that remains is overhead door.





**CUNNINGHAM  
G R O U P**

*AIA Minnesota  
Firm Award Recipient*



**INFORMATION OR ACTION REQUIRED**

---

**END OF OBSERVATION REPORT 23**
