

Architect's Observation Report

Report: 11
Date: August 8, 2014
Time: 3:31 pm
Temp: 78 Degrees
Weather: Partially Cloudy



*AIA Minnesota
Firm Award Recipient*

Project: 13-0639 – Edina Sports Dome and Ice Rink
Owner: City Of Edina
Architect: Cunningham Group Architecture Inc.
Copy To: File

Conformance with Schedule: On Schedule

Present at Site (Observed):

- | | |
|--|--|
| <input checked="" type="checkbox"/> Dale Michalek(RJM) | <input checked="" type="checkbox"/> Ann Kattreh |
| <input checked="" type="checkbox"/> Dan Mehok (RJM) | <input checked="" type="checkbox"/> Susie Miller (City of Edina) |
| <input checked="" type="checkbox"/> Gerhardt Gliège (RJM) | <input checked="" type="checkbox"/> Eric Boettcher (City of Edina) |
| <input checked="" type="checkbox"/> Paul Koliás (RJM) | <input checked="" type="checkbox"/> Amanda Holle (City of Edina) |
| <input checked="" type="checkbox"/> Wyatt Gutzke (New Look PM) | <input checked="" type="checkbox"/> Peter Saabye (City of Edina) |
| <input checked="" type="checkbox"/> Brad Werner (Kelleher PM) | <input checked="" type="checkbox"/> Tunde Olusanya (CGA) |

Cunningham Group
Architecture, Inc.

St. Anthony Main
201 Main Street SE
Suite 325
Minneapolis, MN
55414

Tel: 612 379 3400
Fax: 612 379 4400

WORK IN PROGRESS

1. The last section of grade beam footing was poured today (SW corner), reinforcing bars and formwork is set for grade beam wall which is scheduled to be poured on Monday August 11, 2014. Grade beam should be completed by the subsequent Friday.




www.cunningham.com



CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*

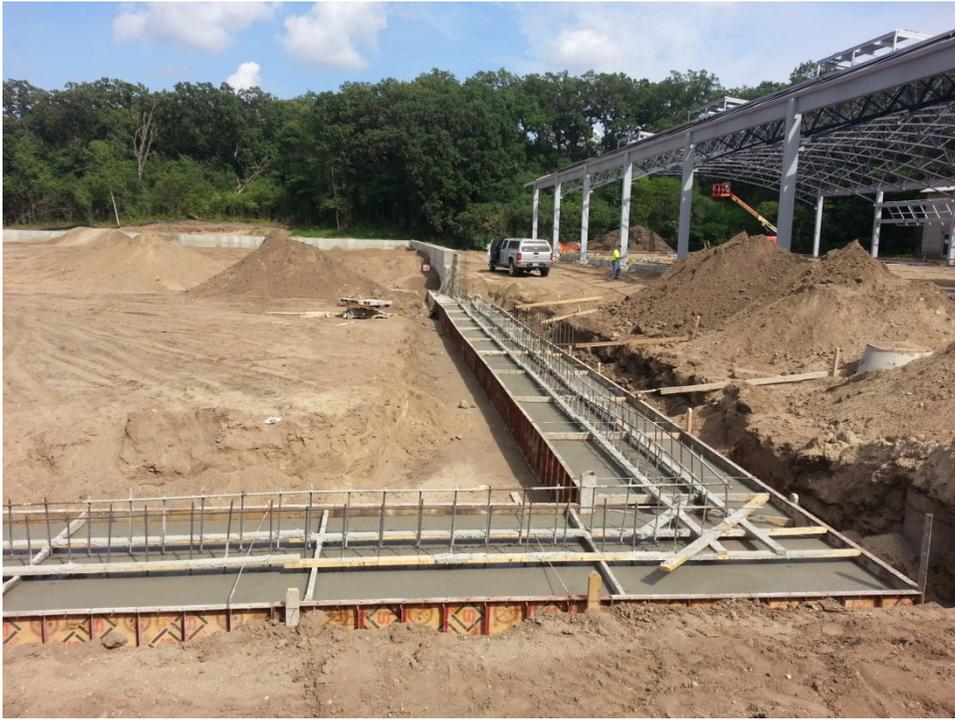



CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*

2. Dome vehicle access has previously been a concern as grade been installation progressed; the solution provided has been to go over the grade beam with soil (while protecting it with plywood). Access points are at the North West and south east sides of dome.





CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*



3. Grade beam interior grading set at bottom of dome drainage system is currently in progress.





CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*

4. West retaining big block wall installation big block and regular block installation is complete (additional course has been added)





CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*



5. Steel decking for ice rink roof deck installation is currently in progress. Roof deck outrigger and edge angle installation also in progress.





CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*





CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*



6. North wall of east arena Refrigeration room has been exposed, the existing sub grade waterproofing needs to be checked for asbestos before work can continue. If asbestos is found abatement will be required.





CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*

INFORMATION OR ACTION REQUIRED

1. Dome grade beam installation still in progress, grade beam installation is expected to be complete on the Friday August 15, 2014.
2. ~~Pricing for East Arena Mechanical plaza waterproofing has come back, option 1 was selected.~~ Documentation for the proposal request is in progress.

END OF OBSERVATION REPORT 11
