

Architect's Observation Report

Report: 18
Date: September 30, 2014
Time: 3:02 pm
Temp: 54 Degrees
Weather: Mostly clear



CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*

Project: 13-0639 – Edina Sports Dome and Ice Rink
Owner: City Of Edina
Architect: Cunningham Group Architecture Inc.
Copy To: File

Conformance with Schedule: On Schedule

Present at Site (Observed):

| | |
|--|--|
| <input checked="" type="checkbox"/> Dale Michalek(RJM) | <input type="checkbox"/> Ann Kattreh |
| <input checked="" type="checkbox"/> Dan Mehok (RJM) | <input checked="" type="checkbox"/> Susie Miller (City of Edina) |
| <input checked="" type="checkbox"/> Gerhardt Gliège (RJM) | <input checked="" type="checkbox"/> Eric Boettcher (City of Edina) |
| <input checked="" type="checkbox"/> Rob Madden (Muska) | <input type="checkbox"/> Amanda Holle (City of Edina) |
| <input checked="" type="checkbox"/> Wyatt Gutzke (New Look PM) | <input checked="" type="checkbox"/> Dave Green (Yeadon) |
| <input checked="" type="checkbox"/> Brad Werner (Kelleher PM) | <input checked="" type="checkbox"/> Tunde Olusanya (CGA) |

**Cunningham Group
Architecture, Inc.**

St. Anthony Main
201 Main Street SE
Suite 325
Minneapolis, MN
55414

Tel: 612 379 3400
Fax: 612 379 4400

WORK IN PROGRESS

1. Turf installation is ongoing, laying cutting and rolling of turf currently in progress.



www.cunningham.com



CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*





**CUNNINGHAM
G R O U P**

*AIA Minnesota
Firm Award Recipient*



2. Accessory building CMU wall installation is still in progress, overhead soffit steel framing work is currently in progress. Some sub grade plumbing piping and some conduit installation and electric panels work has been performed.





**CUNNINGHAM
G R O U P**

*AIA Minnesota
Firm Award Recipient*





CUNNINGHAM
G R O U P


*AIA Minnesota
Firm Award Recipient*





CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*

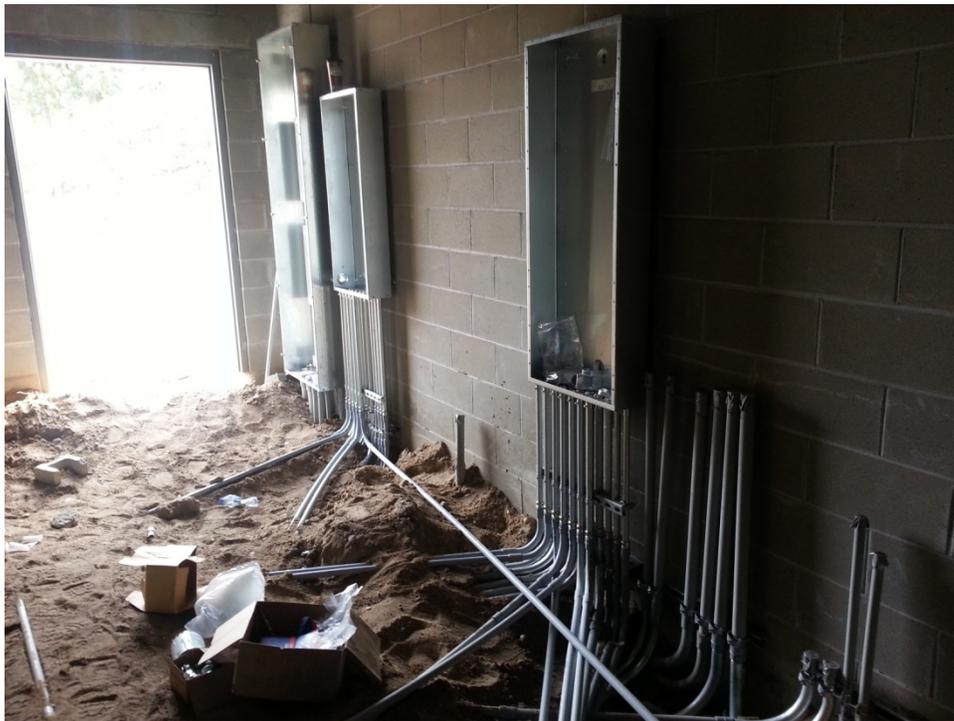



CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*





CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*

3. Retaining wall seat walls on the west side of dome installation is complete.





CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*





CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*

4. Ice rink canopy roof installation is in progress as cover board and membrane installation has begun on the north side of the ice rink canopy.





CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*


5. Insulation in ice rink floor has been installed; piping trench excavation has been filled.





**CUNNINGHAM
G R O U P**

*AIA Minnesota
Firm Award Recipient*

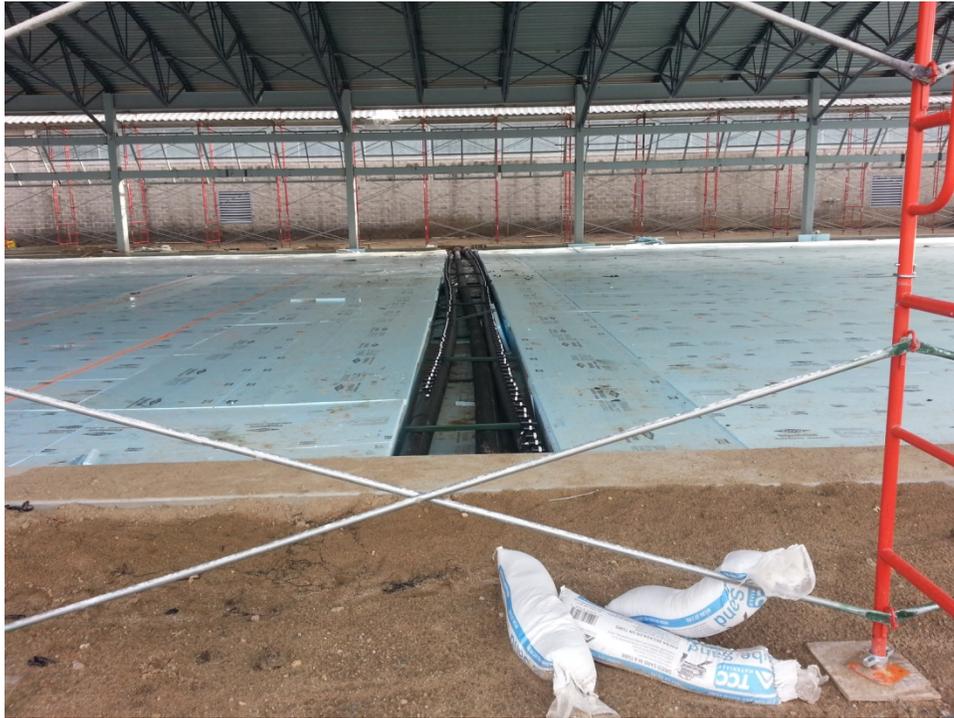

6. Installation of refrigeration room equipment is still ongoing, coordination for electrical conduit, mechanical piping and ductwork ongoing.





**CUNNINGHAM
G R O U P**

*AIA Minnesota
Firm Award Recipient*





CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*



7. Mechanical duct penetrations from restrooms in East Arena to Mechanical Electrical room are being installed. Contractors to coordinate ceiling heights and associated mechanical and electrical elements.





CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*



8. Waste piping lines have been installed in East Arene restrooms in cut slab .






CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*

9. CMU wall in East Arena between team rooms 16 and 17 (just south of the restrooms 26 and 27) has been built, openings for ductwork have been cut.

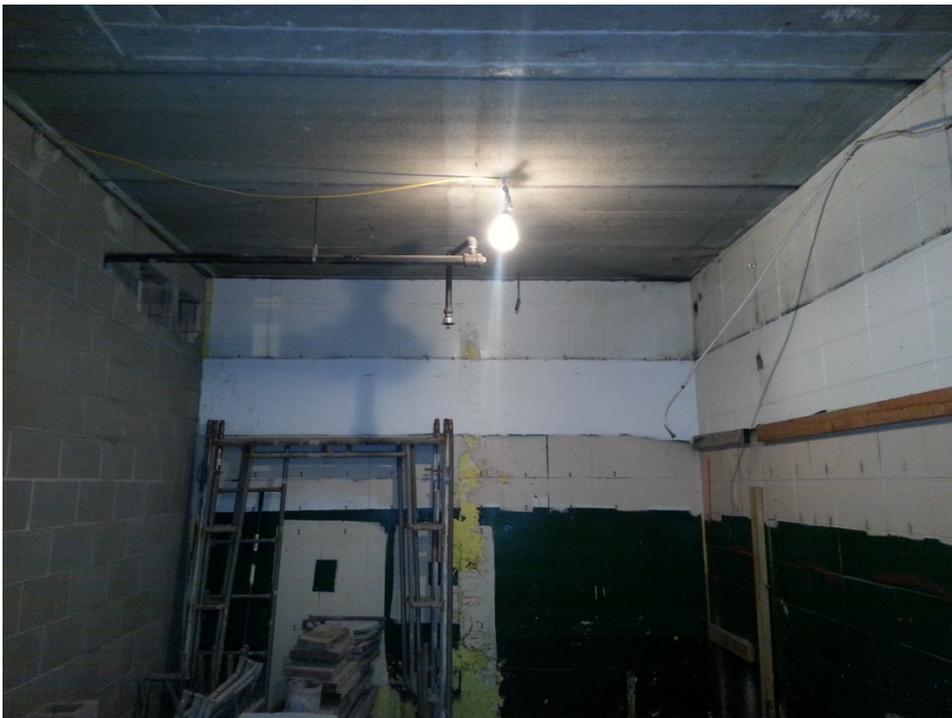



CUNNINGHAM
G R O U P

*AIA Minnesota
Firm Award Recipient*

INFORMATION OR ACTION REQUIRED

1. Ice melt pit outside exterior ice rink design is pending - CGA to issue drawings.
2. ~~East Arena shoring drawings need to be submitted to the City of Edina.~~ **Complete.**

END OF OBSERVATION REPORT 18
