

# Architect's Observation Report

Report: 22  
Date: November 11, 2014  
Time: 2:27 pm  
Temp: 29 Degrees  
Weather: Light snow



*AIA Minnesota  
Firm Award Recipient*

---

Project: 13-0639 – Edina Sports Dome and Ice Rink  
Owner: City Of Edina  
Architect: Cunningham Group Architecture Inc.  
Copy To: File

---

**Conformance with Schedule:** On Schedule (with some adjustments)

**Present at Site (Observed):**

<input checked="" type="checkbox"/> Dale Michalek(RJM)	<input checked="" type="checkbox"/> Ann Kattreh (City of Edina)
<input checked="" type="checkbox"/> Dan Mehok (RJM)	<input checked="" type="checkbox"/> Susie Miller (City of Edina)
<input checked="" type="checkbox"/> Gerhardt Gliedge (RJM)	<input checked="" type="checkbox"/> Rob Madden (Muska)
<input checked="" type="checkbox"/> Paul Koliass (RJM)	<input checked="" type="checkbox"/> Wyatt Gutzke (New Look)
<input checked="" type="checkbox"/> Thomas Hussong	<input checked="" type="checkbox"/> Steve Flanagan (Yeadon)
<input checked="" type="checkbox"/> Mike Rouse (Horowitz)	<input checked="" type="checkbox"/> Tunde Olusanya (CGA)

Cunningham Group  
Architecture, Inc.

St. Anthony Main  
201 Main Street SE  
Suite 325  
Minneapolis, MN  
55414

Tel: 612 379 3400  
Fax: 612 379 4400

---

## WORK IN PROGRESS

---

1. Dome has been inflated, exit doors and personnel airlocks with sloped roof are installed vehicle airlock is still in progress. All ground to receive concrete or asphalt has been covered with blankets which in turn are held down with wood pallets, as a best attempt to protect from frost.



[www.cunningham.com](http://www.cunningham.com)



**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*



2. Accessory building interior CMU installation is almost complete, exterior soffit installation progress is ongoing and light boxes have been installed. Sheet metal for interior ductwork and cold formed metal framing installation is also in progress and scheduled to be complete by the end of this week.





**CUNNINGHAM**  
G R O U P


*AIA Minnesota  
Firm Award Recipient*





**CUNNINGHAM  
G R O U P**


*AIA Minnesota  
Firm Award Recipient*

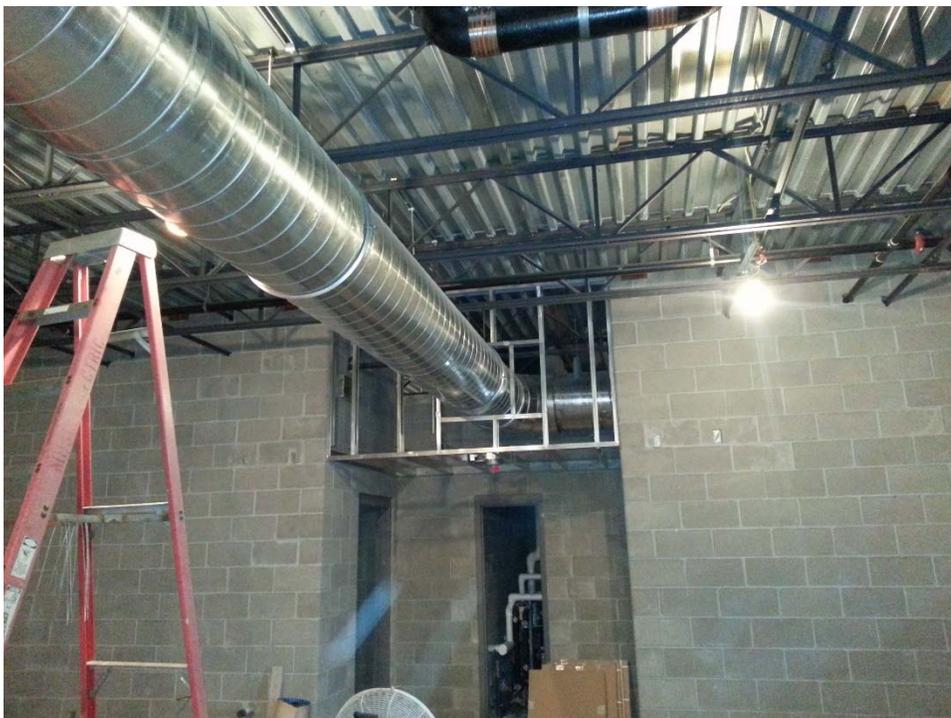



**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

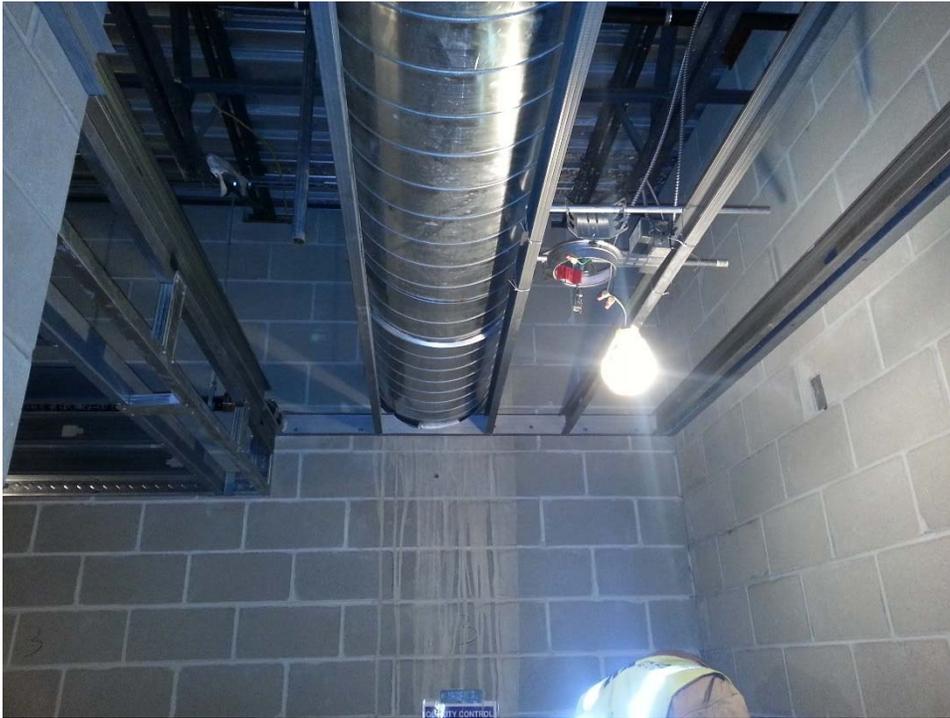



**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

3. Ceiling framing, CMU block installations and pipe fittings for the men's and women's restroom in the East Arena have been installed.






**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*


4. 60% of CMU installation in East Arena is complete, progress in team and locker rooms still ongoing.

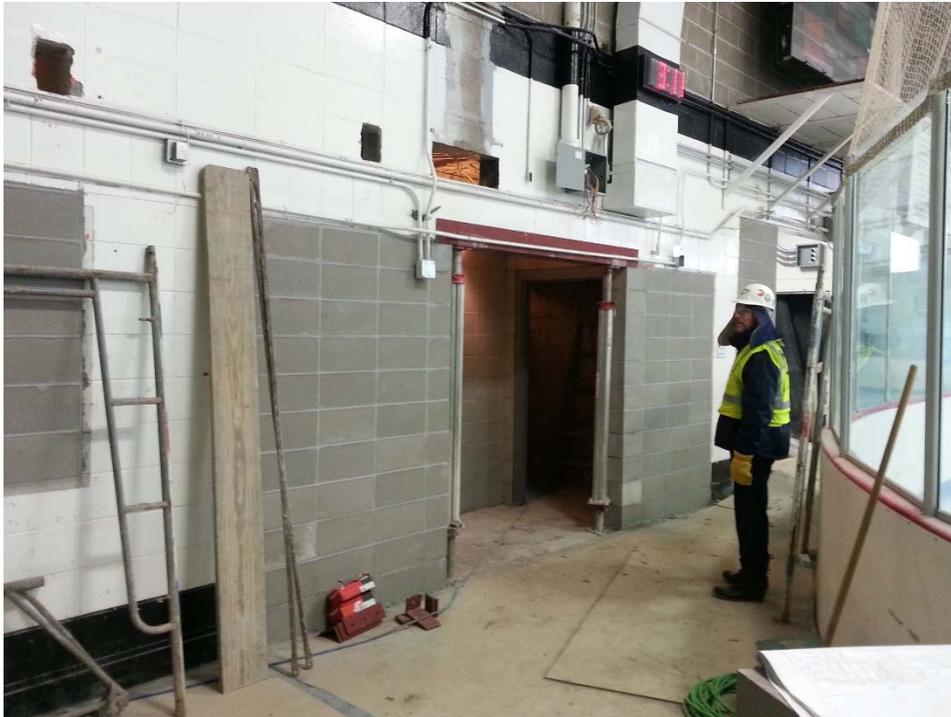



**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

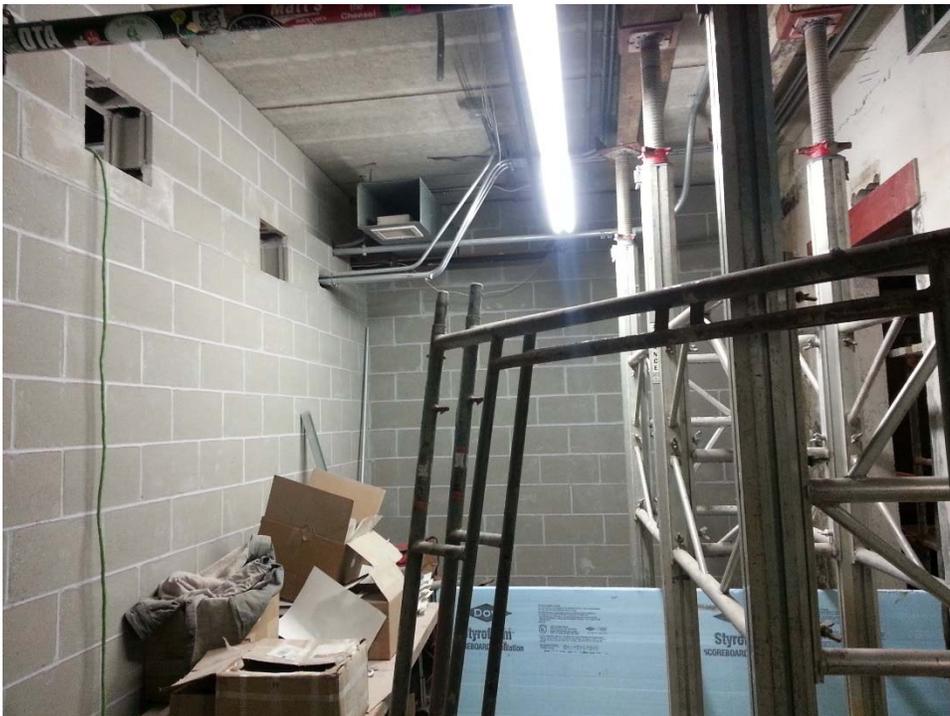



**CUNNINGHAM  
G R O U P**

*AIA Minnesota  
Firm Award Recipient*




**\*\* New storage room\*\***





**CUNNINGHAM  
GROUP**

*AIA Minnesota  
Firm Award Recipient*

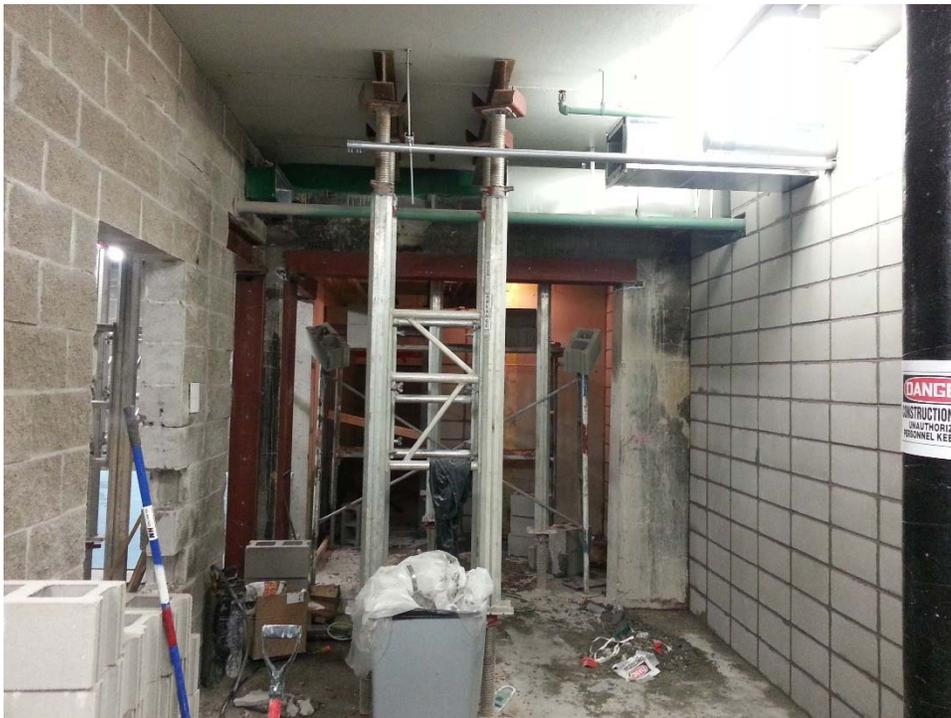



**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

5. Outdoor ice rink slab cover has been removed and dasher board installation has begun





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*



6. Scoreboard wall CMW installation between Ice rink and dome is currently ongoing; the wall is at 4'-0" high.





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

## **INFORMATION OR ACTION REQUIRED**

---

- ~~1. The final revisions for the Mechanical exhaust and intakes from the East Arena Refrigeration room and Mechanical/Electrical rooms are being coordinated—CGA to issue drawings 10/29/14 **Done**~~
- ~~2. RJM to determine if blankets are to be removed from ice rink slab to allow moisture to leave the slab, coordination between Stevens Engineering, Total mechanical and Kelleher recommendations is needed. **Blankets have been removed**~~

**END OF OBSERVATION REPORT 22**
