

# Architect's Observation Report

Report: 03  
Date: June 10, 2014  
Time: 2:36 pm  
Temp: 76 Degrees  
Weather: Sunny



*AIA Minnesota  
Firm Award Recipient*

---

Project: 13-0639 – Edina Sports Dome and Ice Rink  
Owner: City Of Edina  
Architect: Cunningham Group Architecture Inc.  
Copy To: File

---

**Conformance with Schedule: On Schedule**

**Present at Site (Observed):**

- |  |   |
|--|---|
| <input type="checkbox"/> Gerhardt Gliege (RJM)           | <input type="checkbox"/> Ann Kattreh (City of Edina)  |
| <input type="checkbox"/> Dan Mehok (RJM)                 | <input type="checkbox"/> Susie Miller (City of Edina) |
| <input type="checkbox"/> Wyatt Gutzke (New Look PM)      | <input type="checkbox"/> Susan Faus (City of Edina)   |
| <input type="checkbox"/> Jason (New Look Superintendent) | <input type="checkbox"/> Jay Pomeroy (AJA)            |
| <input type="checkbox"/> New Look Superintendent (Water) | <input type="checkbox"/> Tunde Olusanya (CGA)         |
| <input type="checkbox"/> Musco PM.                       | <input type="checkbox"/> Rico Sherman (Excel Energy)  |

Cunningham Group  
Architecture, Inc.

St. Anthony Main  
201 Main Street SE  
Suite 325  
Minneapolis, MN  
55414

Tel: 612 379 3400  
Fax: 612 379 4400

---

## WORK IN PROGRESS

---

1. 6" wet-tap, reducer and gate valve connection on west side of the construction site has been completed.




[www.cunningham.com](http://www.cunningham.com)



**CUNNINGHAM  
GROUP**

*AIA Minnesota  
Firm Award Recipient*

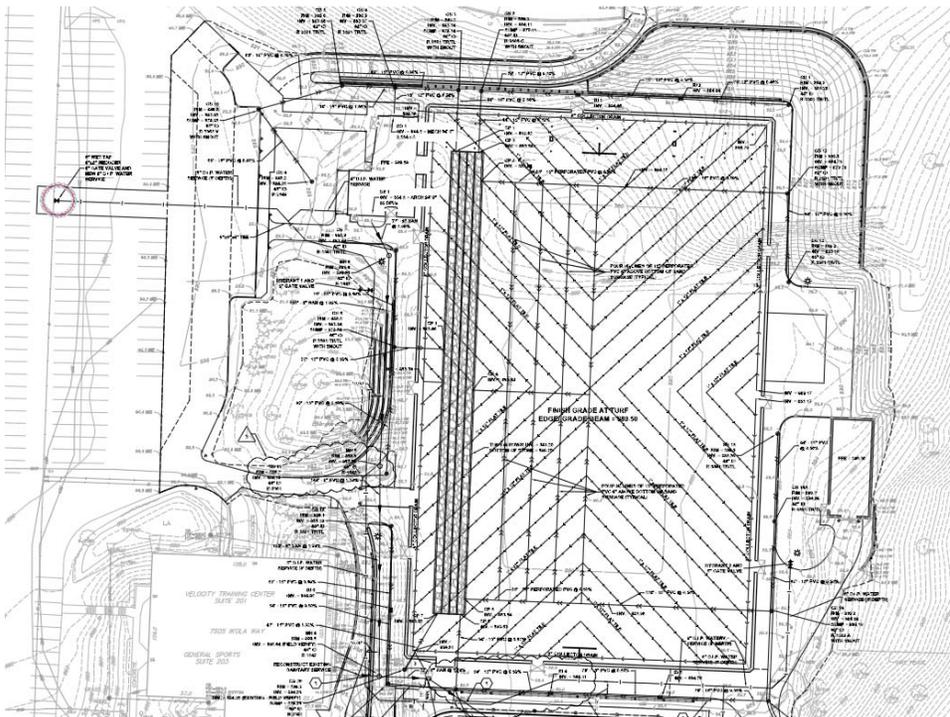


2. 8" Ductile Iron Pipe water service installation has begun at west wet tap installation. Excavation and simultaneous backfill of ductile iron pipe towards project site is ongoing.





**CUNNINGHAM  
GROUP**

*AIA Minnesota  
Firm Award Recipient*

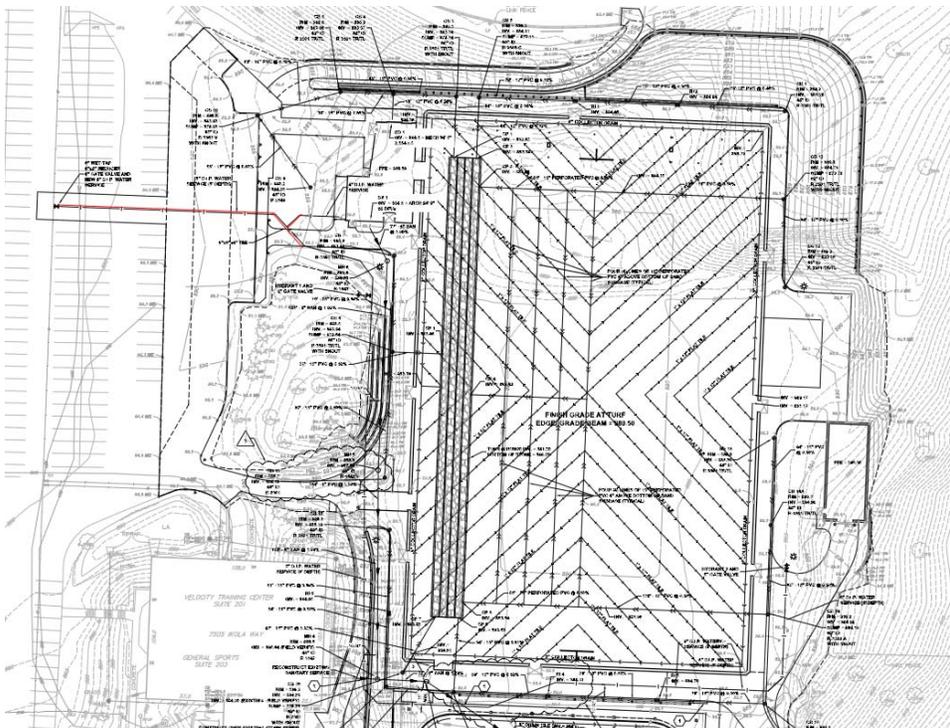



**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

3. Big block retaining wall blocks for the large north retaining wall are currently onsite pending issuance of the retaining wall permit.





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

4. HDPE pipe to be pulled into the directionally drilled hole





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*



5. Directional drill outlet on north side of East Arena is currently being drained and set up to pull HDPE pipe into the directionally bored hole is currently ongoing on south parking lot.





**CUNNINGHAM  
G R O U P**

*AIA Minnesota  
Firm Award Recipient*



6. Gate has been installed on the east side of East Arena.





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

7. 3 Precast concrete manhole installation ongoing and remaining precast manholes/catch basins stored onsite.







**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

8. Hydrant and gate valve assembly currently in progress onsite.





**CUNNINGHAM**  
G R O U P

*AIA Minnesota  
Firm Award Recipient*

## **INFORMATION OR ACTION REQUIRED**

---

1. A Comcast cable line serving the Golf Dome Accessory Building was hit by New Look Construction last week. Dale Michalek to verify that it has been fixed. **Susan Faus to verify if Braemar Golf Dome Cable is still functioning.**
2. Retaining wall permit is also pending, ~~Tunde Olusanya to contact Steve Kiehn to determine Status of permit.~~ **Pending signed special structural testing and inspection schedule.**
3. Directional drill hit an unmarked storm line just East of South Arena; the City of Edina has been notified – repairs to follow.



**END OF OBSERVATION REPORT 03**
